



MR. LOUI LTD.
REPORT "MR. LOUI" VIAREGGIO" JULY 28TH, 2017

M/Y "MR. LOUI"

SUN DECK



- CONTINUED WITH POLISH AND REPAIR DETAILS OF PAINT ON SUN DECK (BAR TABLE, BARBECUE TABLE, DOORS AND ACCESSORIES).



- CONTINUE WITH DETAILS ON TEAK DECK.



- THE STAINLESS STEEL TABLE AND THE TEMPERED GLASS OF LATERAL BARS (PS AND SB) WERE RECEIVED.



UPPER DECK





MR. LOUI LTD.

M/Y "MR. LOUI"

- FRIGOBAR AND ICE MAKER WERE RECEIVED AND INSTALLED.



- CARPENTRY JOBS CONTINUED IN THE SKY SALON, START TO INSTALL ROOF CELING AND TESTING LIGHTS.



- IT FINISHED INSTALLING FLOOR IN SKY SALON.



- START CARPENTRY JOBS IN LOBBY.



- CARPENTRY JOBS CONTINUE ON PILOT HOUSE.





MR. LOUI LTD.

M/Y “MR. LOUI”

- CONTINUE WITH INSTALLATION OF PUMPS AND PVC PIPES ON JACUZZI.



- BOTH SIDES MR LOUI NAMES WERE MOUNTED.




MAIN DECK



- CONTINUE WITH REPAINT AND FIX DETAILS ON AFT DECK.



- CONTINUE WITH INSTALLATION OF TV AND AUDIO RACK, ON THE GALLEY.



- START CARPENTRY JOBS ON SB LOBBY.



MR. LOUI LTD.

M/Y “MR. LOUI”



- THE AFT MR LOUI NAME WAS MOUNTED.



LOWER DECK



- CONTINUE WITH CARPENTRY JOBS IN VIP LOBBY.



- ALL EMERGENCY STEEL WINDOWS WERE INSTALLED.

VIP GUEST CABINS



VIP TWIN CABINS





MR. LOUI LTD. CREW DECK

M/Y "MR. LOUI"



CREW CABINS

- CONTINUE WITH CARPENTRY JOBS.




CREW MESS

- CONTINUE WITH CARPENTRY JOBS. THE DIMENTIONS OF THE SEAT WERE FIX IT.



- CONTINUE WTH CARPENTRY JOBS ON STAIRS TO CREW DECK.



ENGINE ROOM

- CONTINUE TO INSTALLING ROOF CELING.






MR. LOUI LTD.

M/Y "MR. LOUI"

- ALL LED LIGHTS WERE INSTALLED.



- MAIN ENGINE COOLANT DEPOSITS WERE INSTALLED.

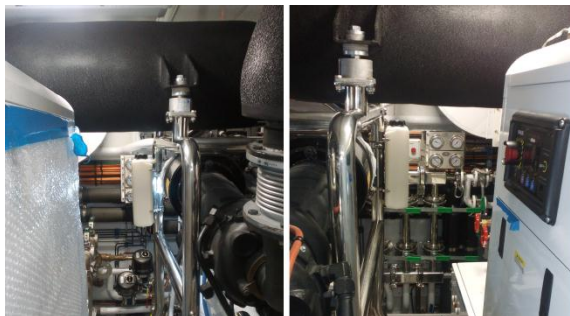

- 3000 LTS. OF MARINE GAS OIL WAS RECEIVED.



HULL AND PROPULSION

- BOTH SIDES SHAFT SEAL PROTECTIONS PLATES, WERE RECEIVED AND PAINTED.





MR. LOUI LTD.

M/Y "MR. LOUI"

- ALL ZINC ANODES WERE INSTALLED ON HULL BOTTOM.



- ALL HULL BOTTOM WAS PAINTED.

